


ID	Task Name	Act. Start	Act. Finish	% Comp.	Phys. % Comp.	Act. Dur.	Rem. Dur.	Act. Cost
1	PEMBINAAN KOLAM TADAHAN BERKONSEPKAN LANDSKAP DAN RUMAH PAM UNTUK MENGELAKKAN BANJIR KILAT DI PERBADANAN PRODUKTIVITI MALAYSIA (MPC) WILAYAH UTARA, KEPALA BATAS, PULAU PINANG	Mon 22-02-21	NA	38%	0%	36.36 days	59.64 days	RM85,455.50
2	SITE POSSESSION	Mon 22-02-21	Mon 22-02-21	100%	0%	1 day	0 days	RM0.00
3	PRELIMINARIES	Mon 22-02-21	NA	38%	0%	36.48 days	59.52 days	RM4,560.00
4	SITE CLEARANCE & EARTHWORK	Mon 22-02-21	Fri 26-02-21	100%	0%	5 days	0 days	RM4,500.00
5	BUILDING WORKS	NA	NA	0%	0%	0 days	56 days	RM0.00
6	Rumah Pam	NA	NA	0%	0%	0 days	56 days	RM0.00
7	Substructure	NA	NA	0%	0%	0 days	21 days	RM0.00
8	Superstructure	NA	NA	0%	0%	0 days	21 days	RM0.00
9	Architecture Works	NA	NA	0%	0%	0 days	21 days	RM0.00
10	EXTERNAL WORKS	Thu 25-02-21	NA	65%	0%	36.4 days	19.6 days	RM28,759.25
11	DETENTION POND	Mon 22-02-21	NA	85%	0%	29.75 days	5.25 days	RM17,123.25
12	MECHANICAL & ELECTRICAL WORKS	Fri 26-02-21	NA	21%	0%	12.18 days	45.82 days	RM30,513.00
13	TESTING & COMMISSIONING	NA	NA	0%	0%	0 days	2 days	RM0.00
14	CLEANING	NA	NA	0%	0%	0 days	2 days	RM0.00
15	HANDOVER	NA	NA	0%	0%	0 days	1 day	RM0.00

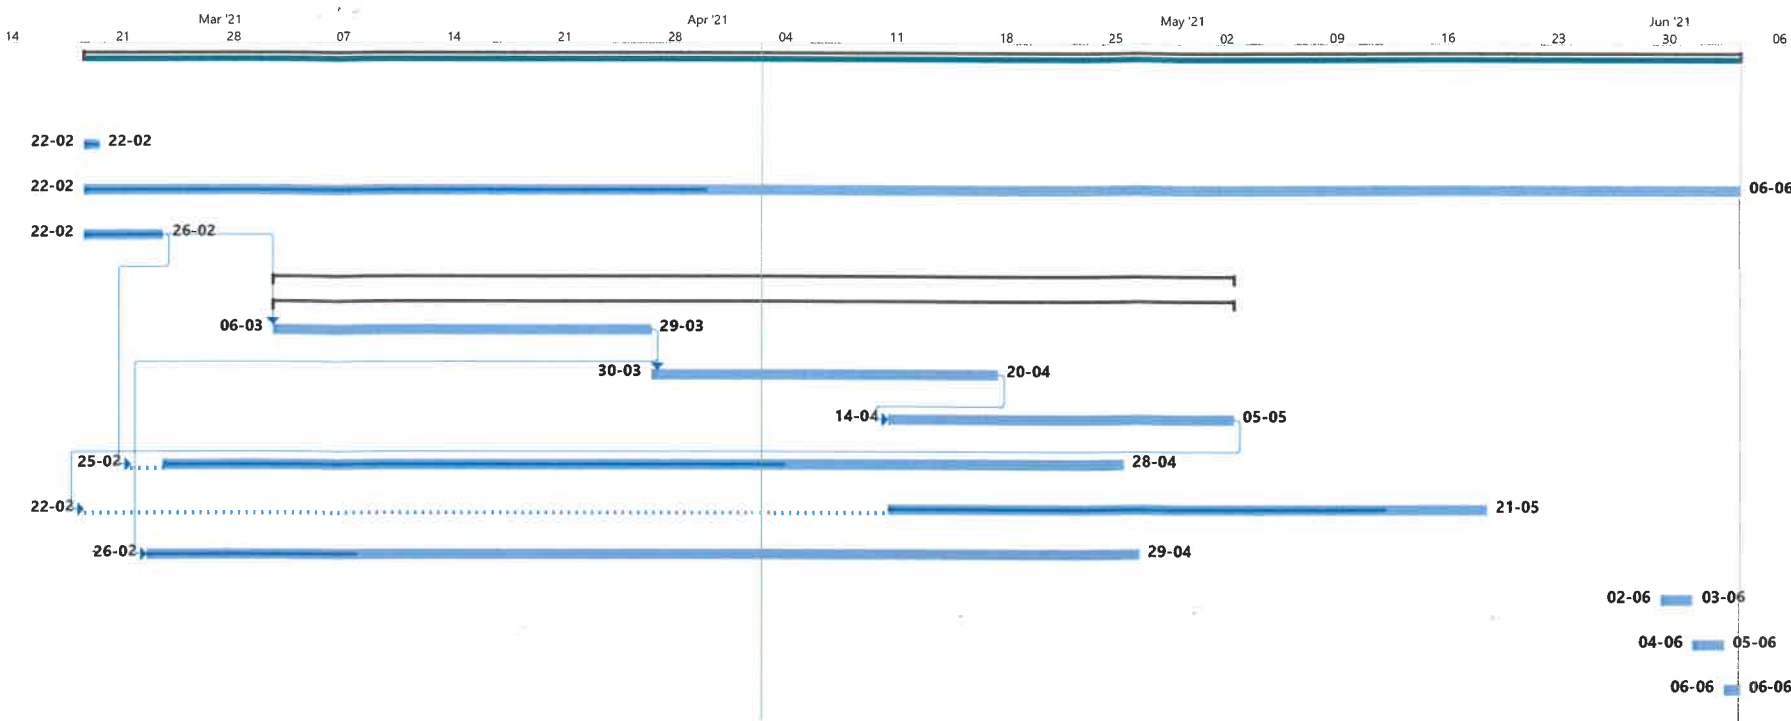

Pembinaan Kolam Tadahan	Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Manual Progress
	Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	
	Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Progress	
