


ID	WBS	Task Name	Duration	Start	Finish	Cost	Actual Start	Actual Finish	% Complete	Actual Cost
1	1	PEMBINAAN KOLAM TADAHAN BERKONSEPKAN LANDSKAP DAN RUMAH PAM UNTUK MENGELOKKAN BANJIR KILAT DI PERBADANAN PRODUKTIVITI MALAYSIA (MPC) WILAYAH UTARA, KEPALA BATAS,	96 days	Mon 22-02-21	Sun 06-06-21	RM284,850.00	Mon 22-02-21	NA	83%	RM228,004...
2	1.1	SITE POSSESSION	1 day	Mon 22-02-21	Mon 22-02-21	RM0.00	Mon 22-02-21	Mon 22-02-21	100%	RM0.00
3	1.2	PRELIMINARIES	96 days	Mon 22-02-21	Sun 06-06-21	RM12,000.00	Mon 22-02-21	NA	90%	RM10,800.00
4	1.3	SITE CLEARANCE & EARTHWORK	5 days	Mon 22-02-21	Fri 26-02-21	RM4,500.00	Mon 22-02-21	Fri 26-02-21	100%	RM4,500.00
5	1.4	BUILDING WORKS	56 days	Sat 06-03-21	Wed 05-05-21	RM57,160.00	Sat 06-03-21	NA	74%	RM39,840.52
6	1.4.1	Rumah Pam	56 days	Sat 06-03-21	Wed 05-05-21	RM57,160.00	Sat 06-03-21	NA	74%	RM39,840.52
7	1.4.1.1	Substructure	21 days	Sat 06-03-21	Mon 29-03-21	RM17,148.00	Sat 06-03-21	Mon 29-03-21	100%	RM17,148.00
8	1.4.1.2	Superstructure	21 days	Tue 30-03-21	Tue 20-04-21	RM17,148.00	Tue 30-03-21	NA	95%	RM16,290.60
9	1.4.1.3	Architecture Works	21 days	Wed 14-04-21	Wed 05-05-21	RM22,864.00	Wed 14-04-21	NA	28%	RM6,401.92
10	1.5	EXTERNAL WORKS	56 days	Thu 25-02-21	Wed 28-04-21	RM44,245.00	Thu 25-02-21	NA	87%	RM38,493.15
11	1.6	DETENTION POND	35 days	Mon 22-02-21	Fri 21-05-21	RM20,145.00	Mon 22-02-21	NA	90%	RM18,130.50
12	1.7	MECHANICAL & ELECTRICAL WORKS	58 days	Fri 26-02-21	Thu 29-04-21	RM145,300.00	Fri 26-02-21	NA	80%	RM116,240....
13	1.8	TESTING & COMMISSIONING	2 days	Wed 02-06-21	Thu 03-06-21	RM0.00	NA	NA	0%	RM0.00
14	1.9	CLEANING	2 days	Fri 04-06-21	Sat 05-06-21	RM1,500.00	NA	NA	0%	RM0.00
15	1.10	HANDOVER	1 day	Sun 06-06-21	Sun 06-06-21	RM0.00	NA	NA	0%	RM0.00

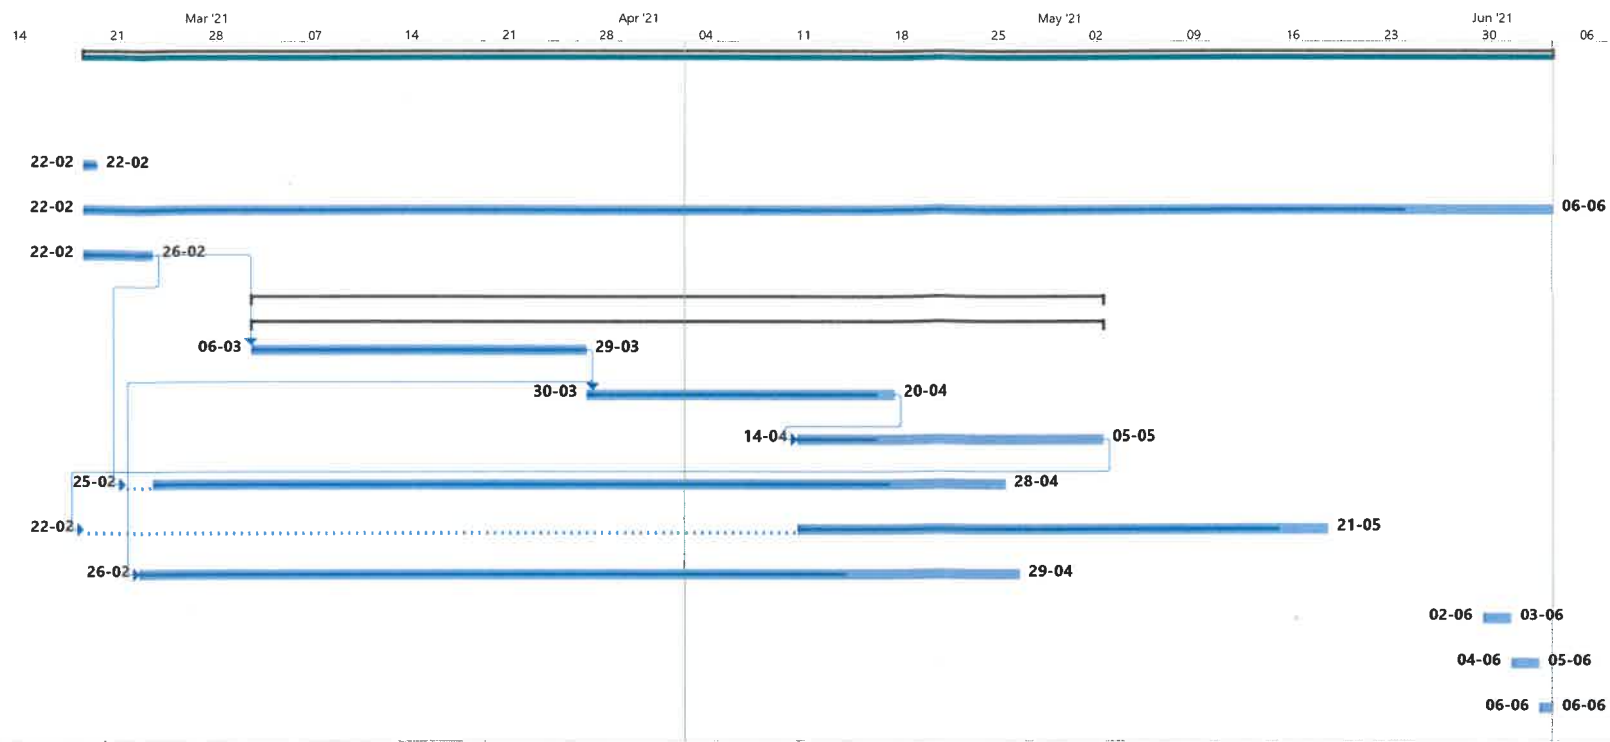

Pembinaan Kolam Tadahan	Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Manual Progress
	Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	
	Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Progress	
